




Clearcreek Road Department

Monthly Report

May 2026

At the beginning of May, crews completed the remaining ditching projects carried over from last year's work list.

Taking advantage of several rainy days, we began repairs to the wash bay wall. Years of salt exposure had caused significant corrosion to the horizontal support beams located at the base and top of the bay door. These beams support the metal siding on both the interior and exterior of the building. The crew replaced approximately 40 feet of both beams and installed new metal siding on the exterior wall.

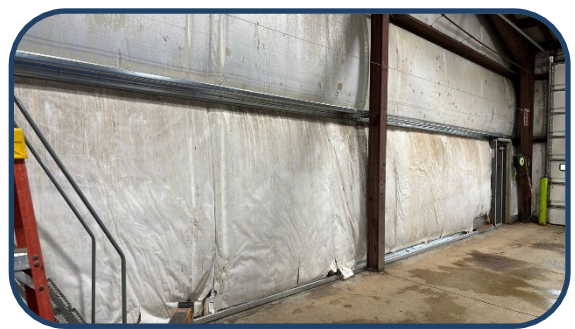

During the second week of May, crews replaced an 18-inch by 35-foot culvert pipe on East Pekin Road in preparation for paving operations.

The crew also began regrouting eight catch basins in the Summit Point subdivision ahead of paving and continued similar work on additional catch basins along Patton Drive.

A sinkhole developed on Meadowview Court during the month. The crew excavated the area and completed the necessary repairs.

The crew also replaced a 36-inch culvert pipe on West Pekin Road with a larger elliptical culvert designed to improve water flow capacity and reduce roadway flooding during heavy rain events. The new culvert measured 38 inches by 58 inches and was 50 feet in length. This project required three days to complete.



**Culvert replacement on
East Pekin Rd.**



**Sink hole on
Meadowview Ct.**



Culvert replacement on West Pekin Rd.



Milling operations began in mid-May and required extensive base repair work in several subdivisions. Significant repairs were completed at:

- Winding Creek (Crooked Creek Drive) – one large base repair area
- Summit Point – five base repair locations
- Cypress Ridge – three base repair locations

Many of these repairs were substantial in size, averaging up to 80 feet in length and 10 feet in width. In total, the department placed 176 tons of asphalt for base repairs and culvert replacement projects during May. For reference, each single-axle dump truck load carries approximately 10 tons of asphalt.

